

FDOT District 5 - Deland Operations Office
 1650 N. Kepler Road Deland, FL 32724
 Phone (386) 740-3548
 Fax (386) 736-5469
 Deland Operations Engineer Ron Mead, P.E.

PROJECT STATUS REPORT AS OF

SEPT 2014

POIPA	CSS	Volusia and Seminole Counties						
		SR 415 from Seminole Co. Line to Reed Ellis Road						
Terry Simpson	Seth Simpson	FIN #	407355-3-52-01, 240216-5-52-01, & 407355-1-52-01					
		Contract #	T5415					
		CONVENTIONAL CONTRACT						
		Project Description: Add lanes & reconstruct.						
		CONTRACTOR:	United Infrastructure Group, Inc.	LET DATE:	5/23/2012	ORIGINAL	1100	\$32,798,973.37
		CCEI:	AECOM	NTP:	7/27/2012	CURRENT	1199	\$33,196,960.74
		CONT. TYPE:	CONSTRUCTION	TIME BEGAN:	10/1/2012	ELAPSED	686	\$23,389,480.11
		FED. AID #:	N/A	WORK BEGAN:	10/1/2012	% ORIGINAL	62.4%	71.3%
		SECTION:	79120000	EST. COMPLETION:	1/12/2015	% TO DATE	57.2%	70.5%
		FUND TYPE	STA	CURRENT CPPR:	96%	LIQ. DAMAGES		
Phone:						Email:		
CONTRACTOR'S PROJECT MANAGER:		Steve Kullman	407-377-0550 O; 803-445-0245 C		Steve.Kullman@uiq.net			
CONTRACTOR'S SUPERINTENDENT:		Joe Walters	407-377-0550 O; 843-415-2171 C		Joe.Walters@uiq.net			
SENIOR PROJECT ENGINEER:		Harold Dubon, P.E.	407-302-6943 O; 407-729-7339 C		Harold.Dubon@aecom.com			
OFFICE SPECIALIST:		Seth Simpson	407-302-6943 Office AECOM		seth.simpson@aecom.com			
CEI SENIOR PROJECT ADMINISTRATOR:		Terry Simpson	407-302-6943 O; 407-622-9476		terry.simpson@aecom.com			
SENIOR INSPECTOR:		Frank Shaw	407-302-6943 O; 407-314-7417 C		Frank.Shaw2@aecom.com			
INSPECTOR:		Jim Cerar	407-302-6943 O; 407-314-8931 C		James.Cerar@aecom.com			
INSPECTOR:		Dominic Fiandra	407-301-6943 O; 407-340-1806 C		Dominic.Fiandra@aecom.com			
MAINTENANCE CONTACT:		Jim Read	386-740-3406 O; 386-801-5584 C		james.read@dot.state.fl.us			
24 HR CONTRACTOR MOT CONTACT:		Joe Walters	407-377-0550 O; 843-415-2171 C					
WEEKLY MEETING: Tuesday 10:00 at AECOM field Office.								
VOLUSIA COUNTY & FLAGLER								
SR 415 from north of Reed Ellis Rd. northerly to north of Acorn Lake Rd.								
FIN #	407355-4-52-01							
Contract #	T-5417							
CONVENTIONAL CONTRACT								
Project Description: Adding lanes, reconstruction, milling and resurfacing, widening, drainage improvements, new traffic signals, new noise wall, and signing and pavement markings on State Road 415 from north of Reed Ellis Road northerly 5.034 miles to north of Acorn Lake Road.								
CONTRACTOR:	P & S Paving, Inc.	LET DATE:	4/25/2012	ORIGINAL	870	\$18,388,844.65		
CCEI:	In House	NTP:	6/28/2012	CURRENT	941	\$18,388,844.65		
CONT. TYPE:	CONSTRUCTION	TIME BEGAN:	7/16/2012	ELAPSED	763	\$14,066,218.76		
FED. AID #:	N/A	WORK BEGAN:	7/16/2012	% ORIGINAL	87.7%	76.5%		
SECTION:	79120000	EST. COMPLETION:	2/11/2015	% TO DATE	81.1%	76.5%		
FUND TYPE	STA	CURRENT CPPR:	100%	LIQ. DAMAGES				
Phone:						Email:		
CONTRACTOR'S PROJECT MANAGER:		Brian Davidson	386-258-7911 O; 386-566-0551 C		bdavidson@gandspavinginc.com			
CONTRACTOR'S SUPERINTENDENT:		Mike Smith	386-402-5705					
CONSTRUCTION ENGINEER		Paul Wabi, P.E.	(386)740-3594 O; 407-625-3055 C		paul.wabi@dot.state.fl.us			
PROJECT ADMINISTRATOR:		Bob Mangogna	407-285-7950		robert.mangogna@dot.state.fl.us			
Consultant LEAD INSPECTOR:		Ray Budd (RS&H)	386-931-8354 C					
INSPECTOR:		Jeremy Ahmann	321-281-7739					
INSPECTOR:								
MAINTENANCE CONTACT:		Jim Read	386-740-3406 O; 386-801-5584		james.read@dot.state.fl.us			
24 HR CONTRACTOR MOT CONTACT:		Mike Smith	386-402-5705					
Bi Weekly Meeting: Wednesday 2:00 On Site								

Bob Mangogna
Jeff Hinkle

FDOT District 5 - Deland Operations Office
 1650 N. Kepler Road Deland, Fl. 32724
 Phone (386) 740-3548
 Fax (386) 736-5469
 Deland Operations Engineer Ron Mead, P E

I-4 from SR 44 to E of I-95

FIN # 408464-1-52-01

Contract # E5R16

DESIGN BUILD CONTRACT

Project Description:

The improvements under this contract consist of reconstruction and widening the interstate from four lanes to six lanes. Additional scope of work includes resurfacing SR 44 eastbound ramps onto SR 400 and replacement of existing US 92 ramps and ramp bridge over US 92.

				TIME	COST	
CONTRACTOR:	Condotte/de Moya Group	LET DATE:	2/3/2012	ORIGINAL	900	\$134,462,000.00
CCEI:	Parsons Brinckerhoff, Inc.	NTP:	5/9/2012	CURRENT	1,208	\$137,707,766.12
CONT. TYPE:	CONSTRUCTION	TIME BEGAN:	5/9/2012	ELAPSED	831	\$87,136,157.04
FED. AID #:	422501	WORK BEGAN:	5/9/2012	% ORIGINAL	92.3%	64.8%
SECTION:	79110000	EST. COMPLETION:	8/29/2015	% TO DATE	68.8%	63.3%
FUND TYPE	FAO	CURRENT CPPR:	92%	LIQ. DAMAGES		

		Phone:	Email:
CONTRACTOR'S PROJECT MANAGER:	Grant Cool	305-322-5597 C; 386-873-0770	grant.cool@demoya.com
CONTRACTOR'S SUPERINTENDENT:	Grant Cool	305-322-5597 C; 386-873-0770	
SUPERVISOR:	Jorge Rodriguez	305-302-6277 C	
CONSTRUCTION ENGINEER	Paul Wabi, P.E.	(386)740-3594 O; 407-625-3055 C	paul.wabi@dot.state.fl.us
CONSTRUCTION PROJECT MANAGER:	Dwight Grube	386-740-3482 O; 386-846-4587 C	dwight.grube@dot.state.fl.us
CEI SENIOR PROJECT ADMINISTRATOR:	Steve Wigle	407-509-8541 C	wigle@pbworld.com
PROJECT ADMINISTRATOR:	Barry Johnson	407-947-7426 C; 386-873-0772 O	johnsonba@pbworld.com
SENIOR INSPECTOR:	Jay Johnson	321-229-9821	
OFFICE SPECIALIST:	Mike Atkins	407-660-4720 O 407-406-1218 C	matkins@metriceng.com
DOT PROJECT MANAGER:	Beata Stys-Palasz	386-943-5418 O	
DOT DESIGN PROJECT MANAGER:	Beata Stys-Palasz	386-943-5418 O	
MAINTENANCE CONTACT:	Jim Read	386-740-3406 O	james.read@dot.state.fl.us
24 HR CONTRACTOR MOT CONTACT:	Grant Cool	305-322-5597 C	

Weekly Meeting: Tuesday, 1:30 at Kepler Complex.

SR 40 Ormond Beach

FIN # 424904-1-52-01, 424904-1-56-01, 418019-152-01

Contract # T5467

LUMP SUM

Project Description: Roadway and Shoulder Wiedening, Milling and Resurfacing, Signalization, Manhole adjustments, SR 40 in Ormond Beach-Tymer Creek Road to Perrott Drive.

				TIME	COST	
CONTRACTOR:	Halifax Paving Inc.	LET DATE:	8/28/2013	ORIGINAL	265	\$4,258,392.00
CCEI:	In House	NTP:	10/31/2013	CURRENT	285	\$4,298,036.18
CONT. TYPE:	CONSTRUCTION	TIME BEGAN:	2/28/2014	ELAPSED	171	\$3,460,167.93
FED. AID #:	NA	WORK BEGAN:	3/1/2014	% ORIGINAL	64.5%	81.3%
SECTION:	79100	EST. COMPLETION:	12/9/2014	% TO DATE	60.0%	80.5%
FUND TYPE	STA	CURRENT CPPR:	98%	LIQ. DAMAGES		

		Phone:	Email:
CONTRACTOR'S PROJECT MANAGER:	Steve Blair	386-676-0200 O; 386-547-3422 C	hpi-steve@cfl.rr.com
CONTRACTOR'S SUPERINTENDENT:	Joseph Durrance	386-676-0200 O; 386-547-4852 C	jdauburn84@aol.com
CONSTRUCTION ENGINEER	Paul Wabi, P.E.	(386)740-3594 O; 407-625-3055 C	paul.wabi@dot.state.fl.us
PROJECT ADMINISTRATOR:	Glenn Raney	386-846-4862 O; 386-846-4862 C	michael.raney@dot.state.fl.us
LEAD INSPECTOR:	Shawn Jackson	386-689-6141	sjackson@rkk.com
MAINTENANCE CONTACT:	Jim Read	(386)740-3406 O; (386)801-5584	james.read@dot.state.fl.us
24 HR CONTRACTOR MOT CONTACT:	Steve Blair	386-676-0200	hpi-steve@cfl.rr.com

WEEKLY MEETING: Wed. on Job Site (AM)

Barry Johnson

Mike Atkins

Glenn Raney

Jeff Hinkle

FDOT District 5 - Deland Operations Office
 1650 N. Kepler Road Deland, Fl. 32724
 Phone (386) 740-3548
 Fax (386) 736-5469
 Deland Operations Engineer Ron Mead, P.E

A1A over Halifax River

Fin # 433262-1-52-01

Contract # E5W15

Project Description: Restoring spalled areas in the bent caps and cathodic protection interal pile jacket intallation to to selected piles

STREAMLINE PLAN QUANTITY CONTRACT

				TIME	COST
CONTRACTOR:	Sieg & Ambachtsheer Inc.	LET DATE:	4/1/2014	ORIGINAL	60 \$ 188,644.00
CCEI:	In House	NTP:	6/11/2014	CURRENT	61 \$ 188,644.00
CONT. TYPE:	Construction	TIME BEGAN:	7/7/2014	ELAPSED	42 \$ 144,936.00
FED. AID #:	NA	WORK BEGAN:	7/7/2014	% ORIGINAL	70.0%
SECTION:	79180	EST. COMPLETION:	9/5/2014	% TO DATE	68.9%
FUND TYPE		CURRENT CPPR:	98%	LIQ. DAMAGES	76.8%

Estimated completion based on pending LD's

		Phone:	Email:
CONTRACTOR'S SUPERINTENDENT:			
CONTRACTOR'S PROJECT MANAGER:	Peiter Ambachtsheer	386-804-1607	pcaus@cflrr.com
CONTRACTOR'S SUPERINTENDENT:	Richard Dean	386-663-5155	
CONSTRUCTION ENGINEER:	Paul Wabi, P.E.	(386)740-3594 O; 407-625-3055 C	paul.wabi@dot.state.fl.us
PROJECT ADMINISTRATOR:	Glenn Raney	386-846-4862 O; 386-846-4862 C	michael.raney@dot.state.fl.us
LEAD INSPECTOR:	Steve Chambers	407-466-1642	steve@jbseng.com
DESIGN PROJECT MANAGER:			
MAINTENANCE CONTACT:	Jim Read	386-740-3406 O	james.read@dot.state.fl.us
MONTHLY CONTACT:			
24 HR CONTRACTOR MOT CONTACT:	Richard Dean	386-663-5155	

Bi Weekly Meeting:

SR 44 Mast Arms Eddie Rd. to 3rd street

FIN # 418020-1-52-01

Contract # T5447

STREAMLINE PLAN QUANTITY CONTRACT

Project Description:

Rebuild 7 signalized intersections to Mast Arms along SR 44 from Eddie Rd. to 3rd. Street in Volusia County

				TIME	COST
CONTRACTOR:	CHINCHOR ELECTRIC INC.	LET DATE:	3/27/2013	ORIGINAL	250 \$ 1,199,934.10
CCEI:	In House	NTP:	6/3/2013	CURRENT	315 \$ 1,199,934.10
CONT. TYPE:	CONSTRUCTION	TIME BEGAN:	10/1/2013	ELAPSED	315 \$ 1,221,092.97
FED. AID #:	N/A	WORK BEGAN:	10/9/2013	% ORIGINAL	126.0%
SECTION:	79070000	EST. COMPLETION:	8/11/2014	% TO DATE	101.8%
FUND TYPE	STA	CURRENT CPPR:	99%	LIQ. DAMAGES	101.8%

		Phone:	Email:
CONTRACTOR'S PROJECT MANAGER:	Brian Silva	1-407-509-2209	bsilva@chinchoelectric.com
CONTRACTOR'S SUPERINTENDENT:	Brian Silva	1-407-509-2209	bsilva@chinchoelectric.com
CONSTRUCTION ENGINEER:	Paul Wabi, P.E.	(386)740-3594 O; 407-625-3055 C	paul.wabi@dot.state.fl.us
PROJECT ADMINISTRATOR:	Chris Kochis	386-740-3503 O; 386-846-3931	chris.kochis@dot.state.fl.us
LEAD INSPECTOR:	Earl Hollister	321-229-6540	ehollister@rkk.com
MAINTENANCE CONTACT:	Jim Read	386-740-3406 O	james.read@dot.state.fl.us
24 HR CONTRACTOR MOT CONTACT:	Jim Zabele	386-561-0165	

Weekly Meeting: Wednesday @ 9:00 AM

Glenn Raney

Jeff Hinkle

Chris Kochis

Jeff Hinkle

FDOT District 5 - Deland Operations Office
 1650 N. Kepler Road Deland, Fl. 32724
 Phone (386) 740-3548
 Fax (386) 736-5469
 Deland Operations Engineer Ron Mead, P E

US 1 SR5 Flagler County Installation of Scour Countermeasures

Fin # 433537-1-52-01
Contract # E5W20

STREAMLINE LUMP SUM CONTRACT

Project Description: Installation of scour countermeasures at US 1 (SR 5) over Hulett Branch Bridge Nos. 730007 and 730044

				TIME	COST	
CONTRACTOR:	AMROAD, LLC	LET DATE:	2/14/2014	ORIGINAL	30	\$95,060.00
CCEI:	In House	NTP:	4/24/2014	CURRENT	45	\$95,060.00
CONT. TYPE:	CONSTRUCTION	TIME BEGAN:	7/7/2014	ELAPSED	42	
FED. AID #:	NA	WORK BEGAN:	7/7/2014	% ORIGINAL	140.0%	0.0%
SECTION:	73010000	EST. COMPLETION:	8/5/2014	% TO DATE	93.3%	0.0%
FUND TYPE	EXO	CURRENT CPPR:	71%	LIQ. DAMAGES		

		Phone:	Email:
CONTRACTOR'S PROJECT MANAGER:	Alejandro Parod, P.E.	305-481-2085	a.pardo@amroadfl.com
CONTRACTOR'S SUPERINTENDENT:	Marcelo Darosa	305-481-3710	
CONSTRUCTION ENGINEER	Paul Wabi, P.E.	(386)740-3594 O; 407-625-3055 C	paul.wabi@dot.state.fl.us
PROJECT ADMINISTRATOR:	John Bailey	407-466-4387	john.bailey@kisingercampo.com
LEAD INSPECTOR:	Tom Grandizio	904-325-0033	thomas.grandizio@rsaandh.com
MAINTENANCE CONTACT:	Jim Read	386-740-3406 O; 386-801-5584 C	james.read@dot.state.fl.us
24 HR CONTRACTOR MOT CONTACT:	Marcelo Darosa	305-481-3710	

Bi Weekly Meeting:

John Bailey
 Ernie Saitar

FDOT District 5 - Deland Operations Office
 1650 N. Kepler Road Deland, Fl. 32724
 Phone (386) 740-3548
 Fax (386) 736-5469
 Deland Operations Engineer Ron Mead, P.E

John Bailey Jeff Hinkle	E. Washington Ave. Sidewalk Improvements						
	Fin # 43018225201						
	Contract # T5505						
	STREAMLINE LUMP SUM CONTRACT						
	Project Description: Project consists of constructing sidewalk handrail, driveways, and signing and pavement markings on Washington Avenue from SR 15 (US 17) to North Pine Street in volusia County						
					TIME	COST	
	CONTRACTOR:	Built Rite Construction Company	LET DATE:	4/30/2014	ORIGINAL	30	\$124,000.00
	CCEI:	In House	NTP:	7/1/2014	CURRENT	47	\$131,512.00
	CONT. TYPE:	CONSTRUCTION	TIME BEGAN:	7/7/2014	ELAPSED	40	\$131,512.00
	FED. AID #:	4224076C	WORK BEGAN:	7/7/2014	% ORIGINAL	133.3%	106.1%
SECTION:	NA	EST. COMPLETION:	8/15/2014	% TO DATE	85.1%	100.0%	
FUND TYPE	EXO	CURRENT CPPR:	98%	LIQ. DAMAGES			
			Phone:	Email:			
CONTRACTOR'S PROJECT MANAGER:		Richard Large	386-749-0312	brci9@aol.com			
CONTRACTOR'S SUPERINTENDENT:		Brian Joy	386-5279228	brci9@aol.com			
CONSTRUCTION ENGINEER:		Paul Wabi, P.E.	(386)740-3594	paul.wabi@dot.state.fl.us			
PROJECT ADMINISTRATOR:		John Bailey	407-466-4387	john.bailey@kisingercampo.com			
LEAD INSPECTOR:		Brad Morely	386-785-3498	bmorely@rkk.com			
MAINTENANCE CONTACT:		Jim Read	386-740-3406 O; 386-801-5584 C	james.read@dot.state.fl.us			
24 HR CONTRACTOR MOT CONTACT:		Brian Joy	386-5279228	brci9@aol.com			
Bi Weekly Meeting:							
Meeting:							
Terry Phillips Ernie Saltar	US-1 / SR5 Flagler County Mill & Resurface w/ Reconstruction of the SB Lane						
	Fin # 427277-1-52-01 & 428603-1-52-01						
	Contract # T5457						
	LUMP SUM CONTRACT						
	Project Description: Minor widening, partial reconstruction, milling and resurfacing, minor drainage improvements, audible pavement markings						
					TIME	COST	
	CONTRACTOR:	P&S Paving	LET DATE:	4/24/2013	ORIGINAL	400	\$8,326,181.00
	CCEI:	In House	NTP:	5/30/2013	CURRENT	427	\$8,464,733.94
	CONT. TYPE:	CONSTRUCTION	TIME BEGAN:	8/25/2013	ELAPSED	358	\$6,341,210.93
	FED. AID #:	4857052P	WORK BEGAN:	8/26/2013	% ORIGINAL	89.5%	76.2%
SECTION:	73010000	EST. COMPLETION:	10/25/2014	% TO DATE	83.8%	74.9%	
FUND TYPE	STA	CURRENT CFPR:	100%	LIQ. DAMAGES			
			Phone:	Email:			
CONTRACTOR'S PROJECT MANAGER:		Brian Davidson	386-258-7911	bdavidson@pandspavinginc.com			
CONTRACTOR'S SUPERINTENDENT:		John Dunlap	386-566-6267	jd@pandspavinginc.com			
CONSTRUCTION ENGINEER:		Paul Wabi, P.E.	(386)740-3594 O; 407-625-3055 C	paul.wabi@dot.state.fl.us			
PROJECT ADMINISTRATOR:		Terry Phillips	386-740-3564	terry.phillips@dot.state.fl.us			
INSPECTOR:		Sean Nazari	407-468-9763	sean.nazari@rsandh.com			
MAINTENANCE CONTACT:		Jim Read	(386)740-3406 O; (386)801-5584	james.read@dot.state.fl.us			
24 HR CONTRACTOR MOT CONTACT:		John Dunlap	386-566-6267	jd@pandspavinginc.com			
Bi Weekly Meeting:							

FDOT District 5 - Deland Operations Office
 1650 N. Kepler Road Deland, FL 32724
 Phone (386) 740-3548
 Fax (386) 736-5469
 Deland Operations Engineer Ron Mead, P.E.

Terry Phillips Ernie Saiter		SR 100 from I-95 East to A1A						
		Fin # 427232-1-52-01 427232-4-52-01 431067-1-52-01		Contract # T6434				LUMP SUM CONTRACT
Project Description:		Mill and Resurface from I-95 east to bridge repair and new signal installation						
				TIME		COST		
CONTRACTOR:	Halifax Paving Inc.	LET DATE:	5/14/2013	ORIGINAL	290	\$3,828,322.50		
CCEI:	In House	NTP:	6/24/2013	CURRENT	323	\$3,828,322.50		
CONT. TYPE:	CONSTRUCTION	TIME BEGAN:	10/21/2013	ELAPSED	301	\$3,733,598.00		
FED. AID #:	3681015P	WORK BEGAN:	10/21/2013	% ORIGINAL	103.8%	97.5%		
SECTION:	73020000	EST. COMPLETION:	11/8/2014	% TO DATE	93.2%	97.5%		
FUND TYPE	EXO	CURRENT CPPR:	100%	LIQ. DAMAGES				
		Phone:		Email:				
CONTRACTOR'S PROJECT MANAGER:		Steve Blair	386-676-0200	hpi-steve@cfl.rr.com				
CONTRACTOR'S SUPERINTENDENT:								
CONSTRUCTION ENGINEER		Paul Wabi, P.E.	(386)740-3594 O; 407-625-3055 C	paul.wabi@dot.state.fl.us				
PROJECT ADMINISTRATOR:		Terry Phillips	386-740-3564	terry.phillips@dot.state.fl.us				
LEAD INSPECTOR:		Michael Sweinhagen	386-931-1091	michael.sweinhagen@rsandh.com				
MAINTENANCE CONTACT:		Jim Read	(386)740-3406 O; (386)801-5584	james.read@dot.state.fl.us				
24 HR CONTRACTOR MOT CONTACT:								
Weekly Meeting:		SR 400 and SR 5A Nova Rd.						
Chris Kochis Ernie Saiter		SR 400 and SR 5A Nova Rd.						
		Fin # 238002-3-52-23		Contract # E5R76				STREAMLINE PLAN QUAN. CONTRACT
Project Description:		Program Signal Enhancement						
				TIME		COST		
CONTRACTOR:	Chinchor Electric, Inc.	LET DATE:	12/4/2012	ORIGINAL	365	\$524,699.77		
CCEI:	In House	NTP:	5/28/2013	CURRENT	440	\$524,699.77		
CONT. TYPE:	CONSTRUCTION	TIME BEGAN:	5/29/2013	ELAPSED	440	\$516,289.10		
FED. AID #:	N/A	WORK BEGAN:	12/9/2013	% ORIGINAL	120.5%	98.4%		
SECTION:	79070000	EST. COMPLETION:	8/11/2014	% TO DATE	100.0%	98.4%		
FUND TYPE	EXO	CURRENT CPPR:	Push Button	LIQ. DAMAGES	May 1, 1900			
		Phone:		Email:				
CONTRACTOR'S PROJECT MANAGER:		Brian Silva	407-509-2209	bsilva@chinchorelectric.com				
CONTRACTOR'S SUPERINTENDENT:		Jimmy Zabele	386-561-0165	jzabele@chinchorelectric.com				
CONSTRUCTION ENGINEER		Paul Wabi, P.E.	(386)740-3594 O; 407-625-3055 C	paul.wabi@dot.state.fl.us				
PROJECT ADMINISTRATOR:		Chris Kochis	386-740-3503 O; 386-846-3931	chris.kochis@dot.state.fl.us				
LEAD INSPECTOR:		Patrick J Langello	386-931-8617	planqello@eismanrusso.com				
MAINTENANCE CONTACT:		Jim Read	(386)740-3406 O; (386)801-5584	james.read@dot.state.fl.us				
24 HR CONTRACTOR MOT CONTACT:		Randy Lanathan						
Weekly Meeting:		Tuesdays @ 2:00pm Project site						
Chris Kochis Ernie Saiter		US-1 SR 44 & A1A						
		Fin # 429179-1-72-02		Contract # E5Q53				STREAMLINE PLAN QUANTITY CONTRACT
Project Description:		Desilting, Cleaning, Video inspection of Storm Drains						
				TIME		COST		
CONTRACTOR:	ESTEP CONSTRUCTION, INC.	LET DATE:	12/4/2013	ORIGINAL	270	\$279,884.55		
CCEI:	In House	NTP:	2/11/2013	CURRENT	302	\$282,759.55		
CONT. TYPE:	MAINTENANCE	TIME BEGAN:	2/11/2013	ELAPSED	553	\$198,427.85		
FED. AID #:	NA	WORK BEGAN:	2/11/2013	% ORIGINAL	204.8%	70.9%		
SECTION:	Various Locations	EST. COMPLETION:	8/30/2014	% TO DATE	183.1%	70.2%		
FUND TYPE	MC	CURRENT CFPR:	77.77%	LIQ. DAMAGES	(\$242,466.00)			
		251 LD Days		Phone:		Email:		
CONTRACTOR'S PROJECT MANAGER:		Jeffrey Estep	(407)325-5998 C	jeff@estepconstruction.com				
CONTRACTOR'S SUPERINTENDENT:		Bob Hersey	(407)810-4936 C					
CONSTRUCTION ENGINEER		Paul Wabi, P.E.	(386)740-3594 O; 407-625-3055 C	paul.wabi@dot.state.fl.us				
PROJECT ADMINISTRATOR:		Chris Kochis	386-740-3503 O; 386-846-3931	chris.kochis@dot.state.fl.us				
LEAD INSPECTOR:		Jim Reininger	(386)527-3834 C					
MAINTENANCE CONTACT:		Jim Read	(386)740-3406 O; (386)801-5584	james.read@dot.state.fl.us				
24 HR CONTRACTOR MOT CONTACT:		Bob Hersey	(407)810-4936 C					
Bi Weekly Meeting:		Tuesday 9:00 am by Phone						

FDOT District 5 - Deland Operations Office
 1650 N. Kepler Road Deland, Fl. 32724
 Phone (386) 740-3548
 Fax (386) 736-5469
 Deland Operations Engineer Ron Mead, P E

SR 472 and 17/92 Interchange

FIN # 434485-1-72-01

Contract # E5T08

STREAMLINE PLAN QUANTITY CONTRACT

Project Description: Landscaping Rehabilitation at SR 472 and 17/92 Interchange

				TIME	COST
CONTRACTOR:	Groundtek of Central FL, LLC	LET DATE:	1/7/2014	ORIGINAL	1159 \$ 223,352.10
CCEI:	In House	NTP:	4/24/2014	CURRENT	1,171 \$ 223,352.10
CONT. TYPE:	MAINTINANCE	TIME BEGAN:	4/28/2014	ELAPSED	112 \$ 169,738.97
FED. AID #:	N/A	WORK BEGAN:	4/28/2014	% ORIGINAL	9.7% 76.0%
SECTION:	79/Volusia	EST. COMPLETION:	7/9/2017	% TO DATE	9.6% 76.0%
FUND TYPE	MC	CURRENT CFPR:	93%	LIQ. DAMAGES	

		Phone:	Email:
CONTRACTOR'S PROJECT MANAGER:	Gregory Bori	407-877-7473	gregory@groundtek.com
CONTRACTOR'S SUPERINTENDENT:	Kevin Campbell	407-877-7473	kevin@groundtek.com
CONSTRUCTION ENGINEER:	Paul Wabi, P.E.	386-740-3594	paul.wabi@dot.state.fl.us
PROJECT ADMINISTRATOR:	Julian McKinley	386-740-3422	julian.mckinley@dot.state.fl.us
LEAD INSPECTOR:	Julian McKinley	386-740-3422	julian.mckinley@dot.state.fl.us
MAINTENANCE CONTACT:	Jim Read	386-740-3406	james.read@dot.state.fl.us
24 HR CONTRACTOR MOT CONTACT:	Hector Colon	407-355-0571	

Meeting:

SR 15/600 (US 17/92)

Fin # 42798617201

Contract # E5T04

STREAMLINE PLAN QUANTITY CONTRACT

Project Description: lining and cleaning storm drain pipes on SR 15/600 (US 17/92) from St. Johns River to Dirksen Dr.

				TIME	COST
CONTRACTOR:	Shenandoah General Con. Co.	LET DATE:	3/14/2014	ORIGINAL	180 \$1,542,225.80
CCEI:	In House	NTP:	5/9/2014	CURRENT	185 \$1,542,225.80
CONT. TYPE:	Maintenance	TIME BEGAN:	5/23/2014	ELAPSED	87 \$58,687.78
FED. AID #:	NA	WORK BEGAN:	6/9/2014	% ORIGINAL	48.3% 3.8%
SECTION:		EST. COMPLETION:	11/23/2014	% TO DATE	47.0% 3.8%
FUND TYPE	STA	CURRENT CFPR:	86.66%	LIQ. DAMAGES	

		Phone:	Email:
CONTRACTOR'S PROJECT MANAGER:	Louis Woska	386-479-8318	l.woska@shenandoahconstruction.com
CONTRACTOR'S SUPERINTENDENT:	Garrett Kulp		
CONSTRUCTION ENGINEER:	Paul Wabi, P.E.	(386)740-3594 O; 407-625-3055 C	paul.wabi@dot.state.fl.us
PROJECT ADMINISTRATOR:	Terry Phillips	(386)943-5770 O; (386)846-4753 C	terry.phillips@dot.state.fl.us
LEAD INSPECTOR:	Nelson Basco	407-271-5979	nbasco@elipsis.com
MAINTENANCE CONTACT:	Jim Read	386-740-3406 O; 386-801-5584 C	james.read@dot.state.fl.us
24 HR CONTRACTOR MOT CONTACT:			

Julian McKinley

Jeff Hinkle

Terry Phillips

Jeff Hinkle

Septembr 2014 Pushbutton Report

PUSHBUTTON STATUS

COUNTY	SECTION	MP	STATE RD	LIMITS	PROJECT DESCRIPTION	EOR	PROJECT PHASE	CONTRACT	WORK ORDER SENT	COMPLETE	CONTR.
Flagler	73010	5.880	US 1	Seminole Woods Blvd	Install Southbound Flashing Beacon	STROZ	Design Complete	-	-	-	-
Flagler	73020	4.699-4.754	100	at I-95	Add right turn lanes	HNTB	In Design	-	-	-	-
Volusia	79060	19.615	600 (US 92)	SR 5A (Nova Rd)	Curb Ramps	STROZ	Under Construction	5228(E5W14)	7/23/2014	10/25/14	TCD
Volusia	79070	25.170	44	I-95 Ramps	Signal, Advanced Loop and Cabinet Installation	PENTON	Under Construction	5226(E5W12)	4/18/2014	7/21/14	Transcore
Volusia	79070	25.155	44	I-95 SB Off-Ramp to EB SR 44	Adding Loop	PENTON	On Hold				
Volusia	79080	5.111	A1A	Andy Romano Beechfront Park	Mid-Block Pedestrian Crossing	ASPIREON	Design Complete				
Volusia	79100	29.652	40	West of Orchard St.	Left Turn Lane	PENTON	On Hold - Permit				
Volusia	79230		421	Yorktowne Blvd	Left turn lane	TBD					
Volusia	79070-009	0.000	44	I-4 WB On-Ramp	Extend Left Turn Lane	STROZ	Design Complete	-	-	-	-

*River of lakes
Heritage Corridor Board*

*requests your presence
at the
Premiere Screening
of*

There's More to Florida

A high definition DVD celebrating the cultural, historic,
and environmental resources of the River of Lakes Corridor.

October 8, 2014

6 PM

Athens Theatre

124 N. Florida Avenue

DeLand, FL 32730

Light hors d'oeuvres will be served.

Cash bar available.

Casual Attire

RSVP at oceanborder74@bellsouth.net or call 386-985-5363



Regional Trails Corridor Assessment



STAKEHOLDER WORKSHOP

DATE & TIME:

Monday, September 29, 2014
5:00PM to 7:00PM
Presentation at 5:15PM


LOCATION:

Daytona State College
Bergengren Hall, Building 110
1200 W. International Speedway Blvd
Daytona Beach, FL 32114

FORMAT:

Presentation at 5:15PM, followed by questions and open house.

Workshop is free and open to the public.

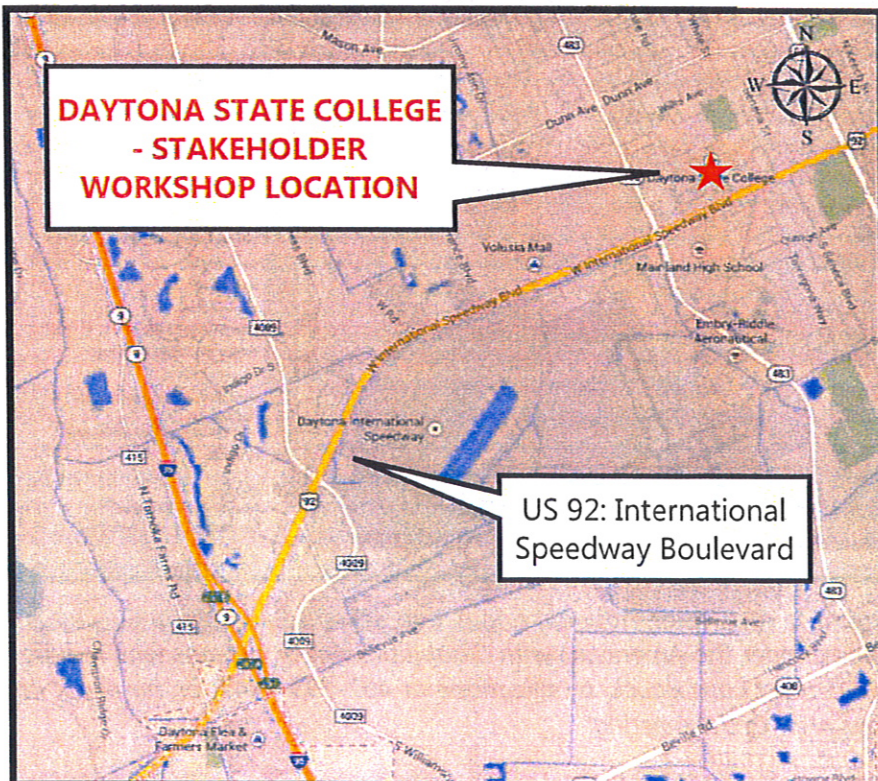


Project Contacts

Lara Bouck - RS&H Project Manager
Phone: 407.893.5847
Email: lara.bouck@rsandh.com

Jean Parlow - TPO Project Manager
Phone: 386.226.0422, ext. 20417
Email: jparlow@r2ctpo.org

PROJECT DESCRIPTION

The River to Sea TPO, in coordination with the Florida Department of Transportation, is undertaking an assessment of regional trails to better understand trail gaps and opportunities for new alignments to be included in the State of Florida Office of Greenways and Trails 2015 update. The goal of this Study is to enhance coordination and better position our region for future funding. For the purposes of this study, a regional trail is a multi-use, paved trail separated from the roadway that is a minimum of 10' wide and crosses, or is intended to cross, through more than one jurisdiction.

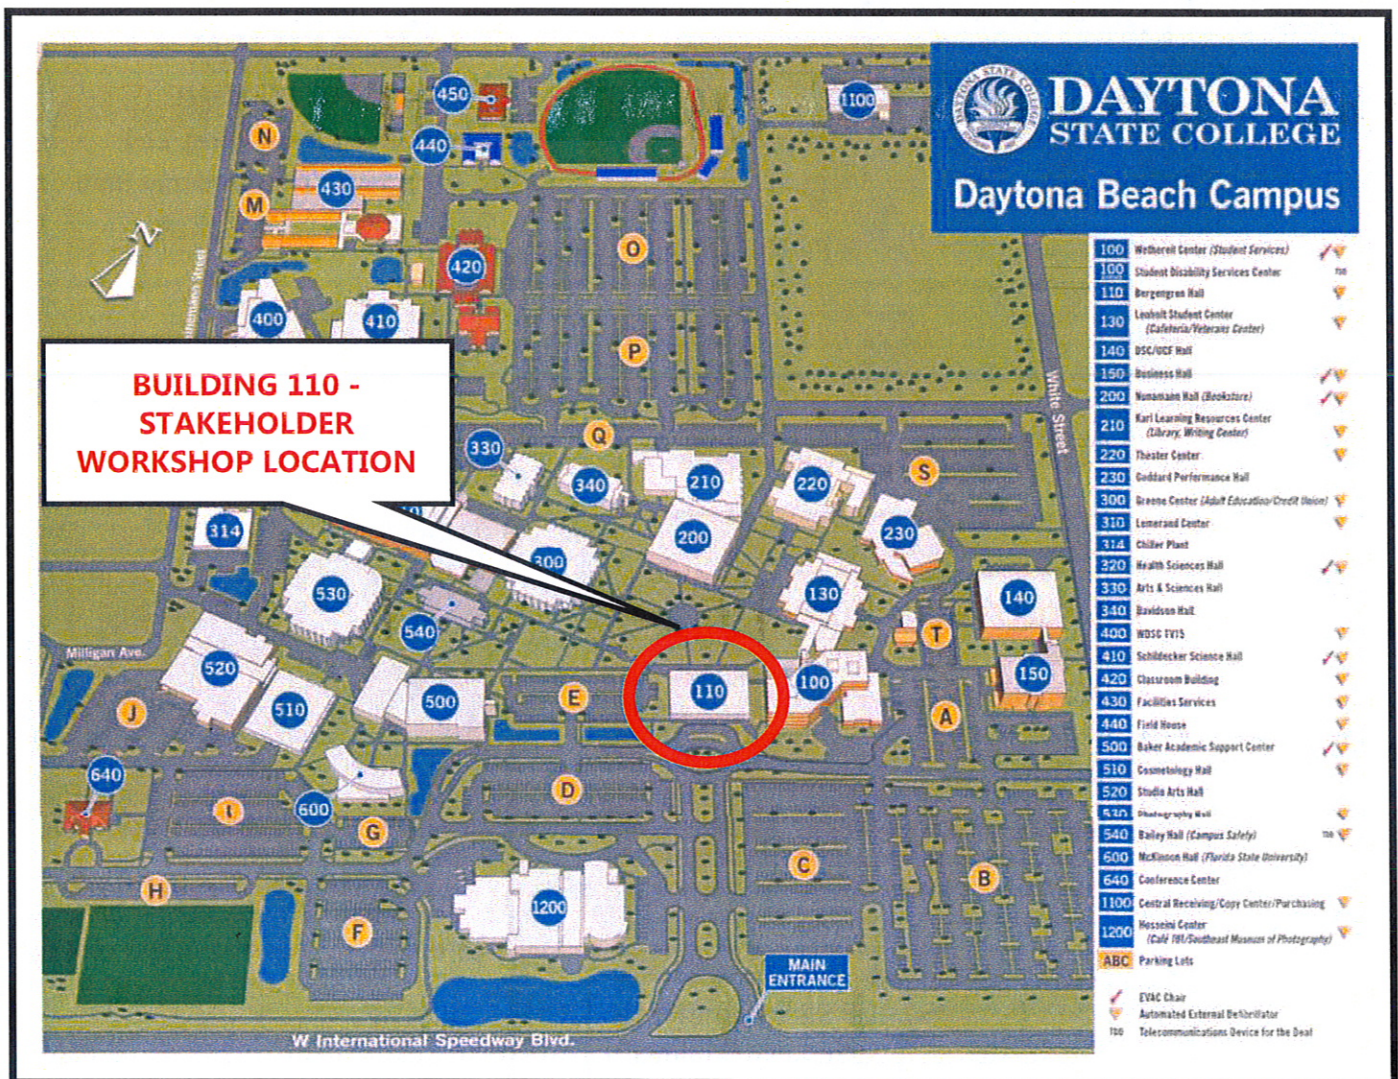

Public participation is solicited without regard to race, color, national origin, age, sex, disability or family status. Persons who require special accommodations under the Americans with Disabilities Act or persons who require translation services (free of charge) should contact Lara Bouck, by telephone at 407-893-5847, or via email at lara.bouck@rsandh.com, at least seven days prior to the meeting.
